


PREPARED BY
TRANSPORTATION & TRANSIT PLANNING & PROGRAMMING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF TRANSPORTATION-BUREAU OF PUBLIC ROADS


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6281
Interstate TRUNK HIGHWAY 35E
COUNTY Ramsey
DISTRICT Metro

LIMITS: E. Jct. T.H. 694 - Ramsey-Anoka Co. Line
Ref. Pt. 114+00.104 - 120+00.382



YEAR BUILT	PROJECT NO	DESCRIPTION			
		TYPE	WIDTH	THICKNESS	REMARKS
C	6281-03	Grading			Divided Highway
		Br. 9562			285' PPG-U.P.
		Br. 9836			195' PPG-U.P.
C	6281-03	Br. 9838			101' PPG U.P.
		Br. 9567 & 9568			Both 256' PPG-U.P.
		Br. 62834			199' PPG-U.P.
C	6281-03	Br. 9592			143' PPG-U.P.
		Br. 62835			194' PPG-U.P.
		Br. 62836			190' PPG-U.P.
C	6281-04	Gravel Base	3'-6"		
		P.C. Concrete	2024' 8'-9"		
		P.I. Mix Bit Shoulders			10' outside & 3' inside
C	-16	TRAFFIC SIGNALS			At Co. Rd. H-2 (C.S.A.H. 5)
C	-17	TRAFFIC SIGNALS			At R.R. BR. NORTH of T.H. 96
M	1982 SF	Sawing Conc. Pymt. Joints			Contract No. 3953
C	6281-35	Bit. Overlay	24'	3"	Spec. 2341 Spec. 2361
C	6281-37	Bit. Overlay	24'	4 1/2"	Spec. 2341
C	6281-38	Bit. Overlay	24'	4 1/2"	Spec. 2361
M	6281	Major Crack Repair			
D	2001 8825-102	Rout & Seal			Spec. 3725
M	2010 8825-378	Bit. Fog Seal			Seal coat Shldr's only
S	6281-23	Grading			
		Bit. Mill & Overlay	24'	2"	
		Concrete Overlay	24'	9"	Unbonded

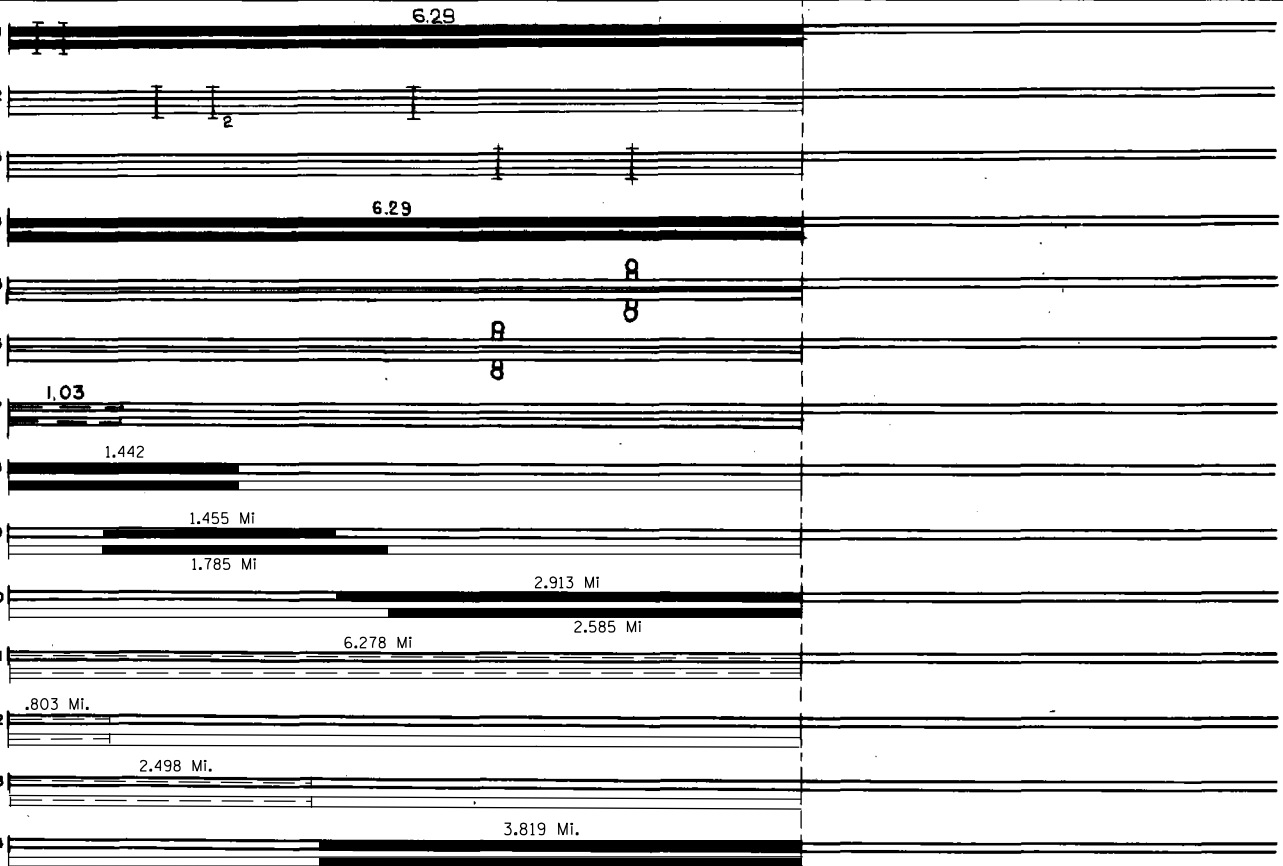

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1970		6.29	2.77	0.00	3.47	0.05	0.00	0.00	6.24	0.05

REMARKS: Layout is to scale as of 1970

