FORM R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1108
TRUNK HIGHWAY 200
COUNTY Cass
DISTRICT 3A

LIMITS: E. Jct. T.H. 6 in Remer - E. Co. Line.

Ref. Pt. 158+00.908 - 167+00.027

PLAN



YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
					No Record of Constr.	
		Gravel	12'	1½"-2"	Added in 1934.	
		Br. 6096	16'		25' B.S.	
1936	34=162-21-1	Grading	32'			
		Gravel	28'	1½"	800 C.Y./Mile.	
		Br. 5622			W10BDX43.	
1938	1108-02	Grading	32'			
		Gravel	28'	1½"	Maint. Dept.	
C						
1942	1108-04	Stab. Grav. Base	30'	6½"		
		Subgr. Corr.				
M						
1948	A.F.E. 24	Repair Stab. Grav. Base			668 C.Y. Clay	
C		Gravel Base	28'-30'	0"-12"	added thickness	
1950	1108-06	Plant Mix Bit.	24'	1½"		
	A.F.E. 27	Install Culvert			48"×60' C.M.	
M		Spot Treat			SC-3, 2309 Gal.	
1960		Bit. Surf. Repair	24'		Agg. 162 Tons	
		Light Bit. Seal	24'		RS-1, 15162 Gal.	
C						
1966	Maint. Proj.	Plant Mix Bit.	24'	1½"		
C						
1979	1108-07	Bit. Surfacing	28'	2½"		
M						
1985	SF	Spot Overlay			Spec. 2331	
C		Bit. Milling	24'	1½"		
1999	1108-08	Bit. Overlay	24'	3"	Spec. 2350	
		Bit. Shoulder	8'	3"	Spec. 2350	
S						
2002	8823-31	Seal Coat			F2	
M						
2003	8823-42	Aggreg. Shldrs.	2'	2"	C5	
M						
2004	8823-52	Bit. Seal Coat	28'		Spec. 2356	

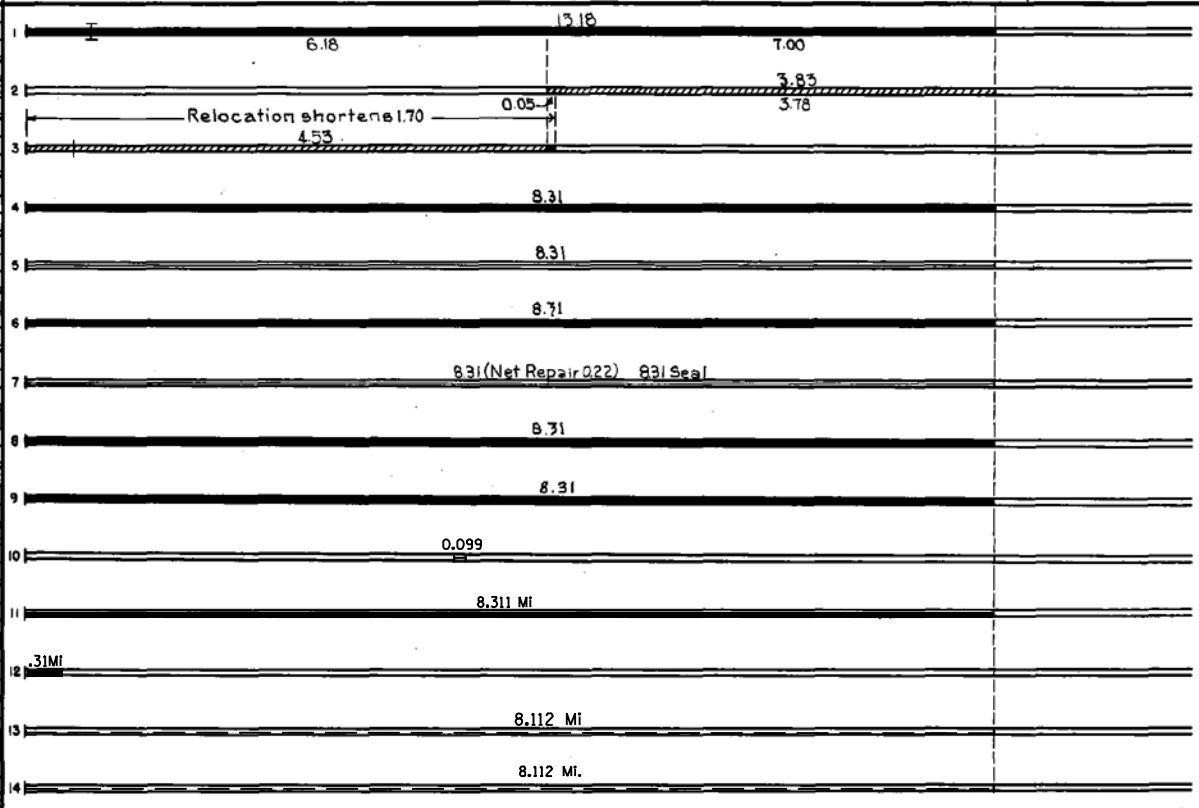

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1934	1935	13.18	12.90	0.01	0.27	0.00	13.17	0.01	0.00	0.00
1936	1937	10.01	9.73	0.01	0.27	0.00	10.00	0.01	0.00	0.00
1938		8.31	8.00	0.00	0.31	0.00	8.31	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1938.
