FORM R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 5207
TRUNK HIGHWAY 99
COUNTY Nicollet
DISTRICT 7A

LIMITS: (In St Peter) N. Jct. T.H. 169 - W. End of Bridge (Minn. River)

Ref. Pt. 013+00.300 - 013+00.415

PLAN



YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
		Gravel			No Record of Constr.	
1930	99-21-21	Concrete	20'		(1)	
C		Milling	24'	3"		
1997	5207-01	Bit. Overlay	66'	Var.	Spec. 2331, 2341	
M		Major				
2001	8827-16	Crack Repair				

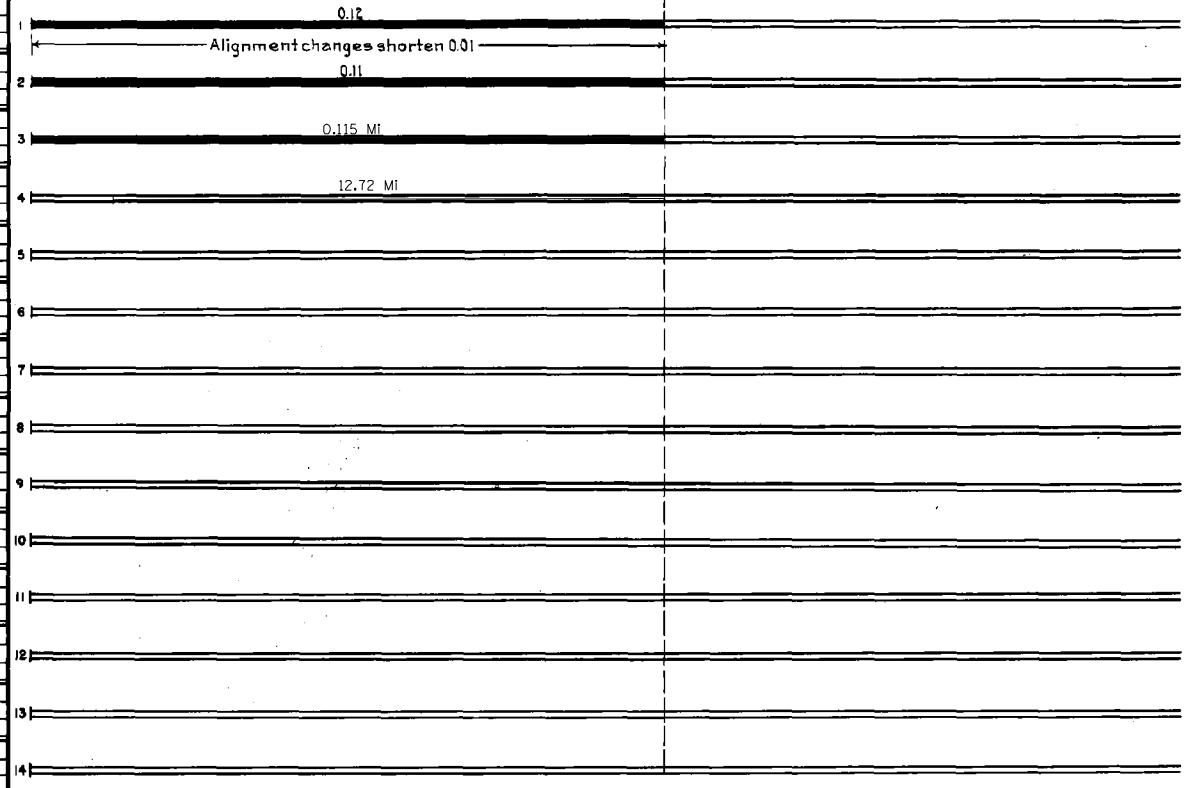

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1921	1929	0.12	0.00	0.00	0.12	0.00	0.00	0.00	0.12	0.00
1930		0.11	0.00	0.00	0.11	0.00	0.00	0.00	0.11	0.00

REMARKS: Layout is to scale as of 1930
(1) 23' Bituminous Rt. & Lt. apparantly placed by city at later date
