FORM R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 7911
TRUNK HIGHWAY 60
COUNTY Wabasha
DISTRICT 6A

LIMITS: Bridge over Mississippi River at Wabasha

Ref. Pt. 219+00.225 - 219+00.458

YEAR BUILT	PROJECT Nº	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
1931 (1)		Br. 4588	19'		H.I. DT.&C.T.G. 2173 Steel&Conc. (515 spans)	
M 1948	7911-02	Misc. Work			Remove Shear Fender Const. Pile Clusters	
M 1965	SF	Light Bit. Seal	24'		Bit. Mix 425 Gal. FA-1 Agg. 14 C.Y.	

PLAN



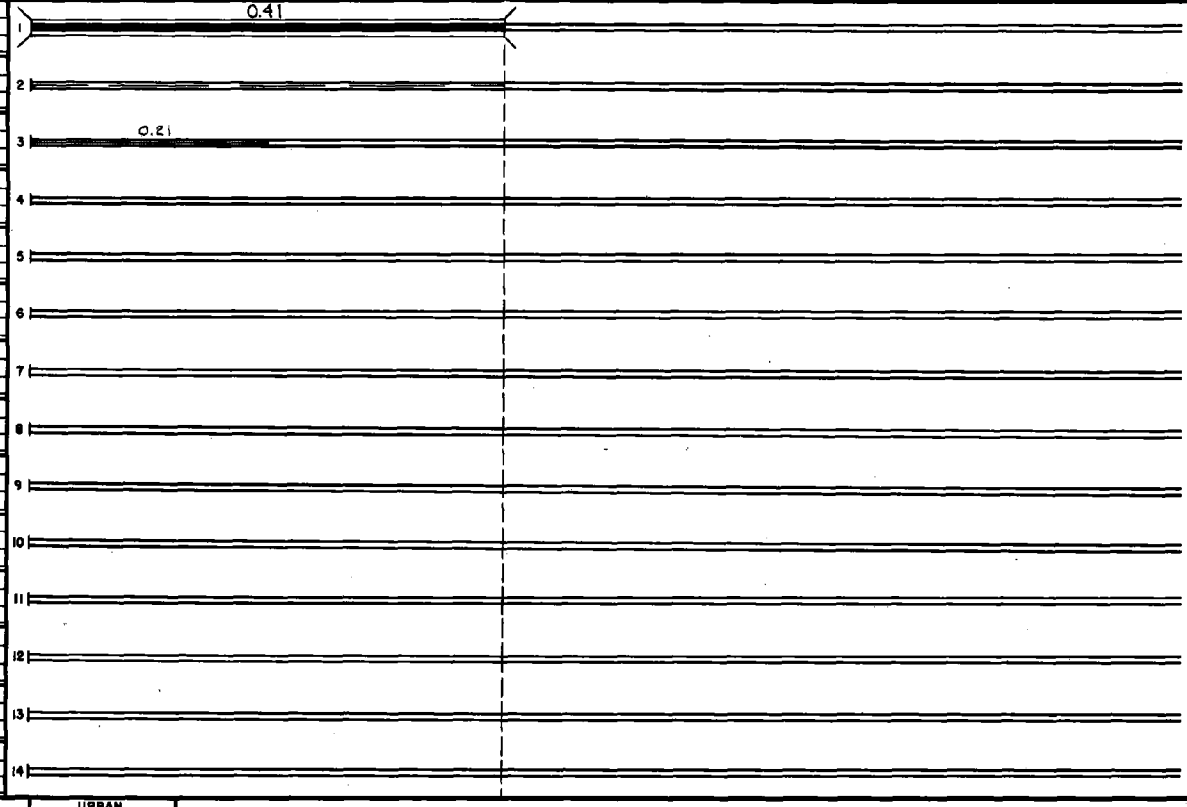

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1947		0.41	0.00	0.00	0.00	0.41	0.00	0.00	0.00	0.41

REMARKS: Layout is to scale as of 1947.
(1) Old Wabasha-Nelson Toll Bridge purchased in 1947.
