FORM R.L.-7 REV. 2-40

SHEET 1 OF 2

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8412
TRUNK HIGHWAY 210
COUNTY Wilkin
DISTRICT 4A

LIMITS: In Breckenridge
E. End of Bridge (Bois des Sioux River)-S. Jct. T.H. 75



YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
1921	3-3-17	Concrete	56			
C 1942	8412-01	State Line Marker			N.Y.A.	
C 1952	8412-03 8412-05	Plant Mix Bit.	56'	3½"		
M 1962		Light Bit. Seal	56'		RS-2, 2274 Gal. Agg. 65 C.Y.	
M 1968	8412-08	Pl. Mix Bit Surf.	56'	5/8"	Bit. Mat'l. 57 Tons	

1 — 0.53
2
3 — 0.53
4 — 0.53
5 — 0.53

See Sheet 2 for Data Subsequent to 1974

6
7
8
9
10
11
12
13
14

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1921		0.55	0.00	0.00	0.55	0.00	0.00	0.00	0.55	0.00

REMARKS: Layout is to scale as of 1921.

4-75

FORM R.L.-7 REV. 7-74

SHEET 2 OF 2

PREPARED BY
TRANSPORTATION PLANNING AND PROGRAMMING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8412
TRUNK HIGHWAY 210
COUNTY Wilkin
DISTRICT 4A

LIMITS: In Breckenridge
E. End of Bridge (Red River of the North) – N. Jct. T.H. 75

Ref. Pt. 000+00.033 - 000+00.219

YEAR BUILT	PROJECT NO	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
C	-10 RF 006-9(34)	Grading Gr. Base, P.C. Conc. A. Mix Bit. Shlders.	24' 10'	8"	
C 1992	8412-14	Groove Conc. Bit. Shouldering		1½"	Spec. 2331
C 2002	8412-15	Bit. Overlay	Var.	Var.	Spec. 2350

PLAN

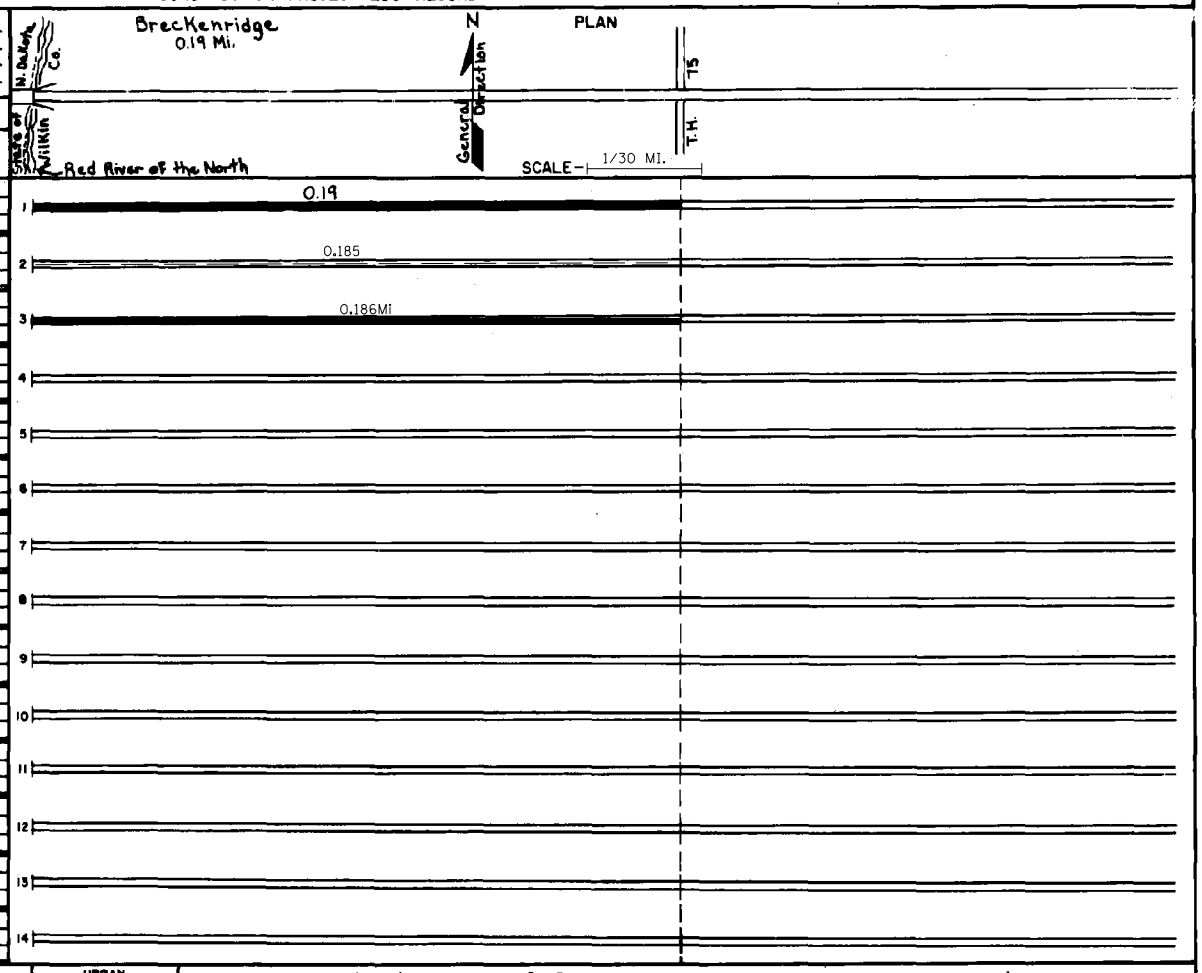

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
		0.19	—	—	0.19	—	—	—	0.19	—

REMARKS: Layout is to scale as of 19
